
	Summary Week Report
---	----------------------------

Project	GiftCase	Week	6
Responsible	Aleksandra Salikiryaki	Date	01.12.2014

Executive Summary

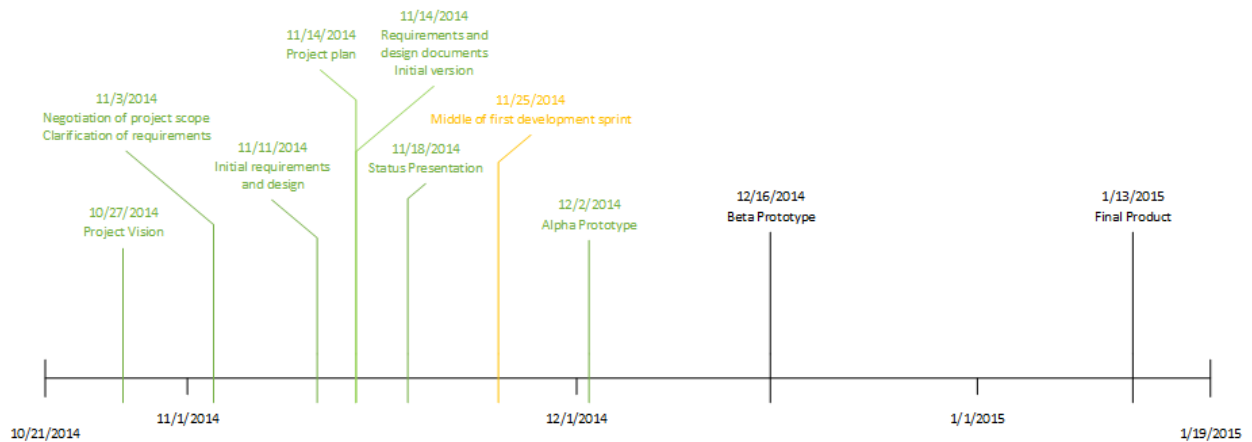

General Project Status	Fulfillment of Next Milestone
on track	slightly behind schedule

Results This Week

Activity Owner(s)	Activity	Workload	Forecast	Result / Comment
All	Preparing the presentation of the Alpha prototype.	3	3	We prepared the presentation for 02 December by meeting on skype and preparing slides. After the slides were completed, we practiced the presentation.

Alexandra Salikiryaki	Adjusting requirements document.	1	1	Adjusting the requirements document according to the client's comments
Gijs Bos	Adjusting the project plan document.	1	1	Filling the missing parts in the project plan document
Gijs Bos, Alexandra Salikiryaki	Upload the code implemented for the front end to the code repository.	1	1	
Gijs Bos, Alexandra Salikiryaki, Giulio Cattivera	Finalize the implementation of the planned views.	6	7	Implemented views - Login view, Main view, Contacts view, Events view
Alexandra Salikiryaki, Giulio Cattivera	Finalize the development of the logical part of the front end application.	6	7	Implementation of the reading of the information from the Back-end REST API. Implementation of the logical models representing the data.
Aleksandra Salikiryaki, Gijs Bos, Giulio Cattivera	Integrate the views with the logical part of the front end application.	6	7	Implementation of the views and controllers used to propagate the information from the logical models to the views.
Ana Stepić	Finalizing REST interface with feedback from front-end development team.	2	2	Removed facebook username from REST parameters. Tuning of some of the other interfaces.
Damir Tomić, Ana Stepić	Integration with content provider for games - Steam.	4	5	Updated steam item conversion. Merged steam categories and regular categories. Updated suggested gift with data from steam.
Damir Tomić, Ana Stepić	Research on the integration with Facebook and the restrictions in getting information. Development of initial integration with Facebook.	4	3	Created Facebook application, set up working facebook log in
Ana Stepić	Set up integration testing environment.	2		

Ana Stepić	Work on the back end.	4	2	Implemented gift controller REST mock up. Set up usage of BaaS json storage service and saving of user data.
Vlatko Klabučar	Telco mockup implementation.	7		Created Telco mockup - a REST application serving as a mockup of Telco data provider and pushed it to GitHub
Vlatko Klabučar	Communication with the client.	2		Discussions of the requirements and the challenges the team meets with the integration with Facebook.

Activities Planned for Next Period

Activity Owner(s)	Activity	Work load	Result / Comment
Giulio Cattivera, Aleksandra Salikiryaki, Gijs Bos	Continue front-end development.	15 (each person)	Implementation of GUI views and functionalities.
Ana Stepić, Vlatko Klabučar	Continuing the development of the back-end.	15 (each person)	Actual implementation of the REST interfaces. Implementation of the integration with content providers, social networks and Telco.
Damir Tomić, Gijs Bos	Recommendation engine research.	8 (each person)	Research and initial ideas for the implementation of the recommending system.
Vlatko Klabučar	Communication with the client.	2	Synchronization of the project status and discussion of problems that we have encountered, like the restrictions in the integration with Facebook.

Action List

Task	Responsible	Comment
Implementation of the remaining views for displaying information (sent, received presents).	Giulio Cattivera, Aleksandra Salikiryaki, Gijs Bos	The static views displaying information should be finished. A strategy for handling the pictures in the application should be developed. The UI should be made more sophisticated.
Implementation of the functionalities proposed by the application (initiate gift proposal, invite user to use GiftCase, login with Facebook).	Giulio Cattivera, Aleksandra Salikiryaki, Gijs Bos	The functionalities related to gift proposal and selection of gift category should be implemented. The possibility to invite a non GiftCase user should be implemented. The integration with Facebook login should be implemented.
Actual implementation of the sending and receiving gifts.	Ana Stepić	The implementation will not include buying of the gifts, but the distribution of gifts among the users.
Integration of Telco mockup REST interface generated by the MDTool with the back-end.	Vlatko Klabučar	

Comments / Experiences / Problems

We have encountered a problem with the restrictions of the Facebook API on gathering data for the users. We are searching for ways to resolve this issue.

Metrics

Milestones

Id	Milestone Description	Responsible Dept./Initials	Finished week				Rem
			Plan	Forecast Week	+/-	Actual	
M-001	Project vision	All	27.10	27.10	0	27.10	0
M-003	Project plan	All	28.10	14.11	17	14.11	0
M-002	Initial requirements and design	All	11.11	11.11	0	11.11	0
M-004	Requirements and design revision	All	14.11	14.11	0	14.11	0
M-005	Alpha prototype	All	01.12	01.12	0	01.12	0
M-006	Beta prototype	All	16.12	16.12			

Working Hours

Member	W1	W2	W3	W4	W5	W6	Total
Gijs Bos	8	5	8	10	8	23	62
Giulio Cattivera	8	5	7	8	11	21	60
Vlatko Klabučar	8	10	8	8	9	12	55
Aleksandra Salikiryaki	8	5	10	10	6	23	62
Ana Stepić	8	7	7	22	6	19	69
Damir Tomić	8	8	7	9	12	11	55
Total	48	40	47	67	52	109	363
