
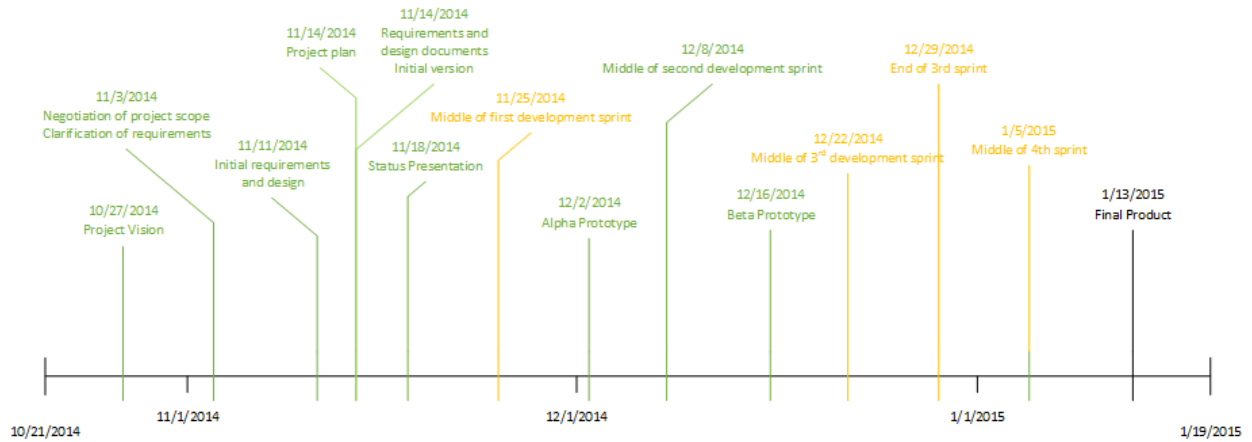
 <b>MÅLARDALEN UNIVERSITY</b> <b>SWEDEN</b>	 <b>POLITECNICO</b> <b>MILANO</b>	<b>Summary Week Report</b>
---	--	----------------------------

Project	GiftCase	Week	11
Responsible	Aleksandra Salikiryaki	Date	05.01.2015

### Executive Summary



General Project Status	Fulfillment of Next Milestone
on track	slightly behind schedule

### Results This Week

Activity Owner(s)	Activity	Workload	Fore cast	Result / Comment
Vlatko Klabučar	Finishing the acceptance test document.	4	4	Finished acceptance test document.
Vlatko Klabučar	Communication with the client and supervisors	1	1	The client and supervisors received our acceptance test plan.

Alexandra Salikiryaki	Implementation of the front-end	4	7	Implemented Facebook login in the Front-end mobile application.
Alexandra Salikiryaki	Setup mobile phone debugging environment	7	7	Executed tests of the application against a mobile device.
All	Writing the weekly report	2	2	Weekly report developed and uploaded
Alexandra Salikiryaki, Gijs Bos, Giulio Cattivera	Synchronization meeting	1		The visual interface of the application was discussed.
Alexandra Salikiryaki, Damir Tomić	Development discussion meeting	1		Discussed changes / problems in the REST API and the related to the Facebook login.
Gijs Bos	Development of visual interface	13	15	Mock-ups for the visual interface of the mobile application have been created.
Damir Tomić	Updating the Facebook provider, upgrading REST functionalities.	7	5	Fetching detailed info from registered GiftCase users, and fetching basic info from unregistered GiftCase users.
Ana Stepić	Work on Push Notifications	4	5	Created google service account and set up push notification service
Ana Stepić	Added Amazon Search by Name	4	5	Implemented Amazon search by item name so we can get item details about items we know user likes and use Amazon recommendation engine for related gift recommendations.

## Activities Planned for Next Period

Activity Owner(s)	Activity	Work load	Result / Comment
Giulio Cattivera, Aleksandra Salikiryaki, Gijs Bos	Continuing the front-end development.	20 (each person)	Continuing implementation of GUI, missing views and missing functionalities. Testing and fixing bugs.
Damir Tomić	Continuing the front-end development. Continue the implementation of the back-end.	15	Continuing implementation of GUI, missing views and missing functionalities. Testing and fixing bugs. Implementation of missing functionalities. Testing and fixing bugs.
Vlatko Klabučar, Ana Stepić	Continue the implementation of the back-end.	15 (each person)	Implementation of missing functionalities. Testing and fixing bugs.
All	Work on the documentation	7 (each person)	Finishing the Design description document.
All	Acceptance testing	3	The application will be tested in accordance with the created acceptance test document.
Vlatko Klabučar	Communication with the client	1	Discussion of the acceptance test plan with the client and the supervisors. Discussion of the starting date for the acceptance tests.
All	Writing the weekly report	2	Development and upload of the weekly report.
All	Synchronization meeting	2 (each person)	
All	Development of final presentation	4	The final presentation will be created and practiced.

## Action List

Task	Responsible	Comment
Continuing implementation of the remaining views for the mobile application.	Giulio Cattivera, Aleksandra Salikiryaki, Gijs Bos	The development of the views for the mobile application will be continued. Some bugs that we have been found and are not yet fixed will be fixed. The GUI for some views like contacts, events, should be made more sophisticated by implementing the mockup views created by Gijs Bos.
Implementation and improvement of the functionalities proposed by the application (downloading gift, buying gift, gift filtering, buying gifts, notifications, filtering gift).	Giulio Cattivera, Aleksandra Salikiryaki, Gijs Bos, Damir Tomić	The functionalities related to downloading gifts, buying gifts should be improved. Notifications should be implemented. A filter for gifts should be implemented.
Testing of the recommendation engine.	Damir Tomić	Different tests of the recommendation engine will be executed in order to guarantee its correct functioning. The eventual bugs will be fixed.
Testing of the REST API.	Vlatko Klabučar	Various tests will be executed against the REST API in order to ensure that all the requests return correct data. The eventual bugs will be fixed.
Adding missing functionalities to the back-end. Testing and fixing bugs in the back-end.	Ana Stepčić	The missing functionalities in the back-end will be implemented. Tests will be executed against the back-end functionalities and eventual bugs will be fixed.

## Comments / Experiences / Problems

The front-end team is still back in the schedule, due to the holidays. Additional effort will be put, in order to ensure that all of the important functionalities will be finished on time.

## Metrics

### Milestones

Id	Milestone Description	Responsible Dept./Initials	Finished week				Rem
			Plan	Forecast Week	+/-	Actual	
M-001	Project vision	All	27.10	27.10	0	27.10	0
M-003	Project plan	All	28.10	14.11	17	14.11	0
M-002	Initial requirements and design	All	11.11	11.11	0	11.11	0
M-004	Requirements and design revision	All	14.11	14.11	0	14.11	0
M-005	Alpha prototype	All	01.12	01.12	0	01.12	0
M-006	Beta prototype	All	16.12	16.12	0	16.12	0
M-007	Acceptance test plan	All	31.12	31.12	0	31.12	0
M-008	Acceptance test report	All	12.01	12.01			

## Working Hours

Member	W1	W2	W3	W4	W5	W6	W7	W8	W9	W10	W11	Total
Gijs Bos	8	5	8	10	8	23	11	15	10	11	14	123
Giulio Cattivera	8	5	7	8	11	21	13	15	14	8	2	112
Vlatko Klabučar	8	10	8	8	9	12	6	13	10	11	7	102
Aleksandra Salikiryaki	8	5	10	10	6	23	15	21	7	10	12	127
Ana Stepić	8	7	7	22	6	19	15	14	12	10	10	130
Damir Tomić	8	8	7	9	12	11	16	16	10	12	9	118
<b>Total</b>	<b>48</b>	<b>40</b>	<b>47</b>	<b>67</b>	<b>52</b>	<b>109</b>	<b>76</b>	<b>94</b>	<b>63</b>	<b>62</b>	<b>54</b>	<b>708</b>
