
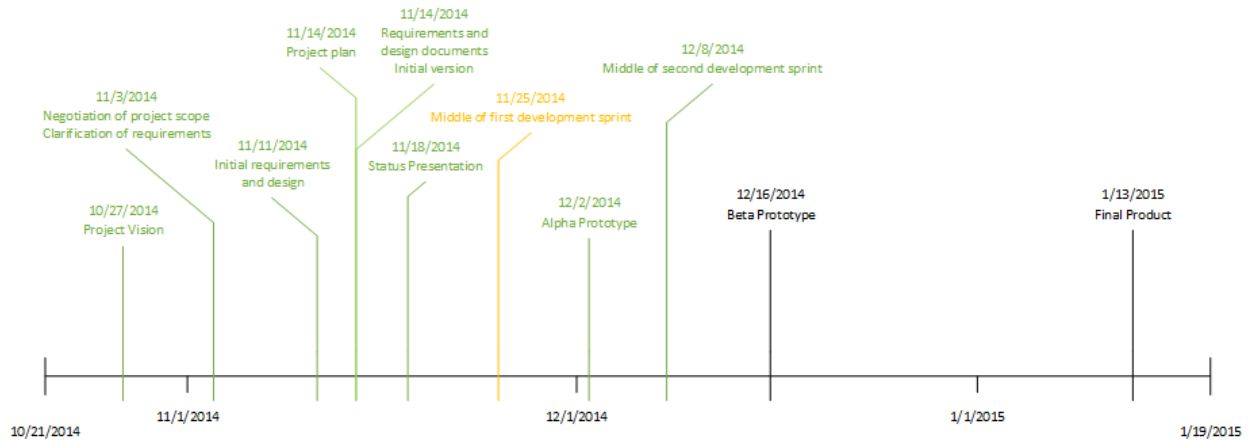
 MÅLARDALEN UNIVERSITY SWEDEN	 POLITECNICO MILANO	Summary Week Report
---	--	----------------------------

Project	GiftCase	Week	7
Responsible	Giulio Cattivera	Date	08.12.2014

Executive Summary



General Project Status	Fulfillment of Next Milestone
on track	slightly behind schedule

Results This Week

Activity Owner(s)	Activity	Workload	Fore cast	Result / Comment
Alexandra Salikiryaki	Front-end progress	15	15	We made the suggested gifts view, inbox and outbox views. Various adjustments.
Giulio Cattivera	Front-end progress	8	8	We made the suggested gifts view, inbox and outbox views. Various adjustments.

Gijs Bos	Front-end progress	5	5	We made the suggested gifts view, inbox and outbox views. Various adjustments.
Giulio Cattivera	Front-end testing	3	3	The prototype was tested on the smartphone and some bugs have been fixed.
Giulio Cattivera	Design document updated	2	2	The part regarding the design of the front-end has been upgraded adding the structure of the application views. Other various fixes have been done.
Ana Stepić	Back-end progress	10	6	Implemented Amazon browsing of Movies, VideoGames, Audio and Related item search, made key fetching from BaaS, continued writing inbox and outbox functionality. Fixed various backend bugs.
Damir Tomić	Back-end progress	3	3	Changed the GiftController so it uses the recommendation engine, rather than hard-coded code. Partially implemented usage of Facebook API likes.
Vlatko Klabučar	Back-end progress	5	3	Added support for fetching TelcoData.
Damir Tomić, Ana Stepić	Back-end progress	5	4	Researched facebook api, permissions, worked on getting extended permissions without review from facebook
Vlatko Klabučar	TelcoMockup adjustment	1	1	Adjusted rest API to serves the needs of backend
Gijs Bos	Working on final documentation	6	4	Improved the documentation, missing chapters, and inconsistencies
Damir Tomić	Back-end progress	8	5	Implemented the recommendation engine, added additional methods to Facebook API.

Activities Planned for Next Period

Activity Owner(s)	Activity	Work load	Result / Comment
Giulio Cattivera, Aleksandra Salikiryaki, Gijs Bos	Continuing the front-end development.	15 (each person)	Continuing implementation of GUI, missing views and missing functionalities.
Vlatko Klabučar, Ana Stepić, Damir Tomić	Continuing implementing the back-end.	15 (each person)	Adding more features to the REST API, implementing database operations.

Action List

Task	Responsible	Comment
Continuing implementation of the remaining views for the mobile application.	Giulio Cattivera, Aleksandra Salikiryaki, Gijs Bos	The development of the views for the mobile application will continue. Some bugs that we have found and are not still fixed will be handled. The GUI for some views like contacts, events, should be made more sophisticated.
Implementation of the functionalities proposed by the application (downloading gifts, facebook real login, buying gifts, various sorting features for gifts and contacts).	Giulio Cattivera, Aleksandra Salikiryaki, Gijs Bos	The functionalities related to downloading gifts, buying gifts should be implemented. The possibility for the user to sort gifts, contacts and filtering features for gifts will be implemented. The integration with Facebook login should be implemented.
Continuing to implement the back-end.	Vlatko Klabučar, Ana Stepić, Damir Tomić	Improving the recommendation algorithm, adding more gift categories, implementing functions for database input/output.

Comments / Experiences / Problems

The week was particularly full of academic commitments for the swedish side and this slowed down a little the progress of the front-end.

Debugging a mobile application continues taking a lot of time, next week we'll set up a more suitable debugging tool.

Backend team encountered problems with Amazon - Amazon account private and public key were put on Github which violates terms of agreement. Old keys needed to be deleted, new keys generated and stored privately where no one can see them.

Metrics

Milestones

Id	Milestone Description	Responsible Dept./Initials	Finished week				Rem
			Plan	Forecast Week	+/-	Actual	
M-001	Project vision	All	27.10	27.10	0	27.10	0
M-003	Project plan	All	28.10	14.11	17	14.11	0
M-002	Initial requirements and design	All	11.11	11.11	0	11.11	0
M-004	Requirements and design revision	All	14.11	14.11	0	14.11	0
M-005	Alpha prototype	All	01.12	01.12	0	01.12	0
M-006	Beta prototype	All	16.12	16.12			

Working Hours

Member	W1	W2	W3	W4	W5	W6	W7	Total
Gijs Bos	8	5	8	10	8	23	11	73
Giulio Cattivera	8	5	7	8	11	21	13	73
Vlatko Klabučar	8	10	8	8	9	12	6	61
Aleksandra Salikiryaki	8	5	10	10	6	23	15	77
Ana Stepić	8	7	7	22	6	19	15	84
Damir Tomić	8	8	7	9	12	11	16	71
Total	48	40	47	67	52	109	76	439
