




# Summary Week Report

Project	GiftCase	Week	13
Responsible	Giulio Cattivera	Date	19.01.2015

## Executive Summary

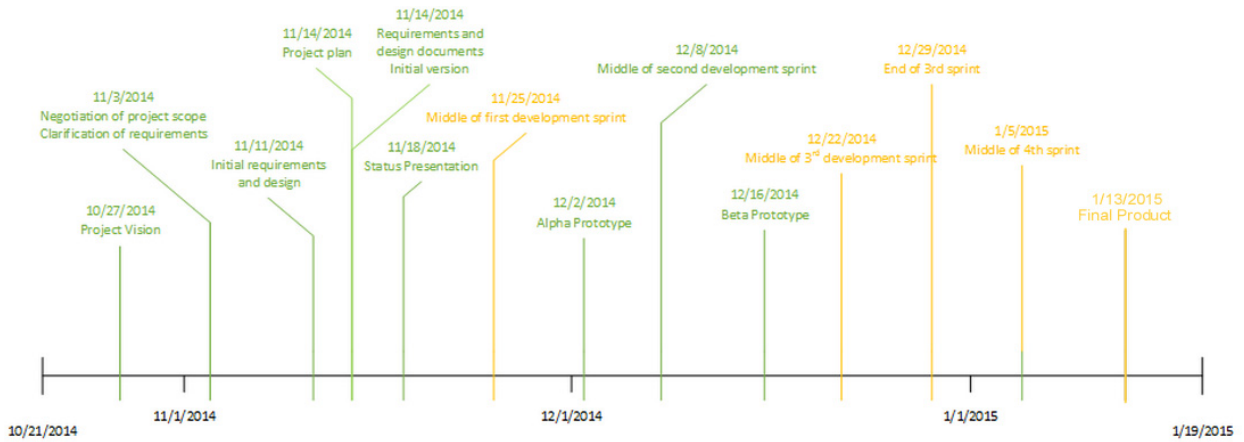

General Project Status	Fulfillment of Next Milestone
finished	finished

## Results This Week

Activity Owner(s)	Activity	Workload	Fore cast	Result / Comment
Gijs Bos, Giulio Cattivera, Vlatko Klabučar	User documentation and final project report	8	6	In finalization of the project, the user documentation had to be written and a final project report had to be created. These activities were performed after our final presentation.
Alexandra Salikiryaki	Remaining front-end features implementation	10		The last work regarding remaining features was carried out.
Ana Stepic, Damir Tomić, Vlatko Klabučar	Remaining tasks on the backend, finalization of the back-end implementation	8	8	As a result of the finalization of the project, some slight modifications and improvements were made in the backend.
Gijs Bos, Giulio Cattivera, Alexandra Salikiryaki	Bug fixing	3	2	The latest manual bug fixing on the front-end app was done.
Alexandra Salikiryaki	Improving the design document	3	2	Some minor improvements to the design document were made

### Activities Planned for Next Period

Activity Owner(s)	Activity	Work load	Result / Comment

### Action List

Task	Responsible	Comment

### Comments / Experiences / Problems

The project is finished and this is the last weekly report so the above sections are missing (Action List, Activities planned for the next period). We look back at a great time of doing a distributed project. We have enjoyed creating our application and want to thank everyone who worked with us. We hope dsd course will continue to educate future students and make them aware of cultural differences and how best practices in software engineering are managed. Thanks a lot to our fabulous team, supervisors, and customer.

### Metrics

#### Milestones

Id	Milestone Description	Responsible Dept./Initials	Finished week				Rem
			Plan	Forecast Week	+/-	Actual	
M-001	Project vision	All	27.10	27.10	0	27.10	0
M-003	Project plan	All	28.10	14.11	17	14.11	0
M-002	Initial requirements and design	All	11.11	11.11	0	11.11	0
M-004	Requirements and design revision	All	14.11	14.11	0	14.11	0
M-005	Alpha prototype	All	01.12	01.12	0	01.12	0
M-006	Beta prototype	All	16.12	16.12	0	16.12	0
M-007	Acceptance test plan	All	31.12	31.12	0	31.12	0
M-008	Acceptance test report	All	12.01	12.01	0	12.01	0

## Working Hours

Member	W1	W2	W3	W4	W5	W6	W7	W8	W9	W10	W11	W12	W13	Total
Gijs Bos	8	5	8	10	8	23	11	15	10	11	14	9	11	142
Giulio Cattivera	8	5	7	8	11	21	13	15	14	8	2	8	11	131
Vlatko Klabučar	8	10	8	8	9	12	6	13	10	11	7	21	16	139
Aleksandra Salikiryaki	8	5	10	10	6	23	15	21	7	10	12	26	16	169
Ana Stepić	8	7	7	22	6	19	15	14	12	10	10	26	8	164
Damir Tomić	8	8	7	9	12	11	16	16	10	12	9	26	8	152
Total	48	40	47	67	52	109	76	94	63	62	54	115	70	897
